

THE CONTINUOUS ELECTRON BEAM ACCELERATOR FACILITY

PROJECT STATUS & PHYSICS OUTLOOK

February 1988

Hermann A. Gruner

THE CONTINUOUS ELECTRON BEAM ACCELERATOR FACILITY: PROJECT STATUS AND PHYSICS OUTLOOK

Hermann A. Grunder *
CEBAF
12000 Jefferson Avenue
Newport News, Virginia 23606

Abstract

Nuclear physics research program planning, accelerator tunnel construction, and accelerator component development, assembly, and testing are under way at the Continuous Electron Beam Accelerator Facility. CEBAF's 4-GeV, 200- μ A superconducting recirculating accelerator will provide cw beam to simultaneous experiments in three end stations for studies of the nuclear many-body system, its quark substructure, and the strong and electroweak interactions governing this form of matter. An experimental program is being defined in collaboration with the user community. Preliminary experimental equipment conceptual designs have been prepared, and the experimental halls have been designed.

Introduction

In February 1987, construction began on the Continuous Electron Beam Accelerator Facility (CEBAF), a laboratory for nuclear physics research in Newport News, Virginia (Figure 1). The accelerator will provide continuous electron beams with energies between 0.5 and 4 GeV and currents up to 200 μ A. CEBAF's purpose is to study the structure of the nuclear many-body system, its quark substructure, and the strong and electroweak interactions governing the behavior of nuclear matter. This requires electron beams of sufficient

- energy to provide the kinematic flexibility required to study the transition region,
- intensity (current) to allow precise measurement of relatively small electromagnetic cross sections,
- duty factor to allow coincidence experiments,
- beam quality to allow high-resolution experiments.

This combination of characteristics—high energy, high current, high duty factor, high beam quality—makes CEBAF a unique tool for nuclear physics research.

* This work was supported by the U.S. Department of Energy under contract DE-AC05-84ER40150. The author acknowledges the technical contributions of CEBAF staff members.

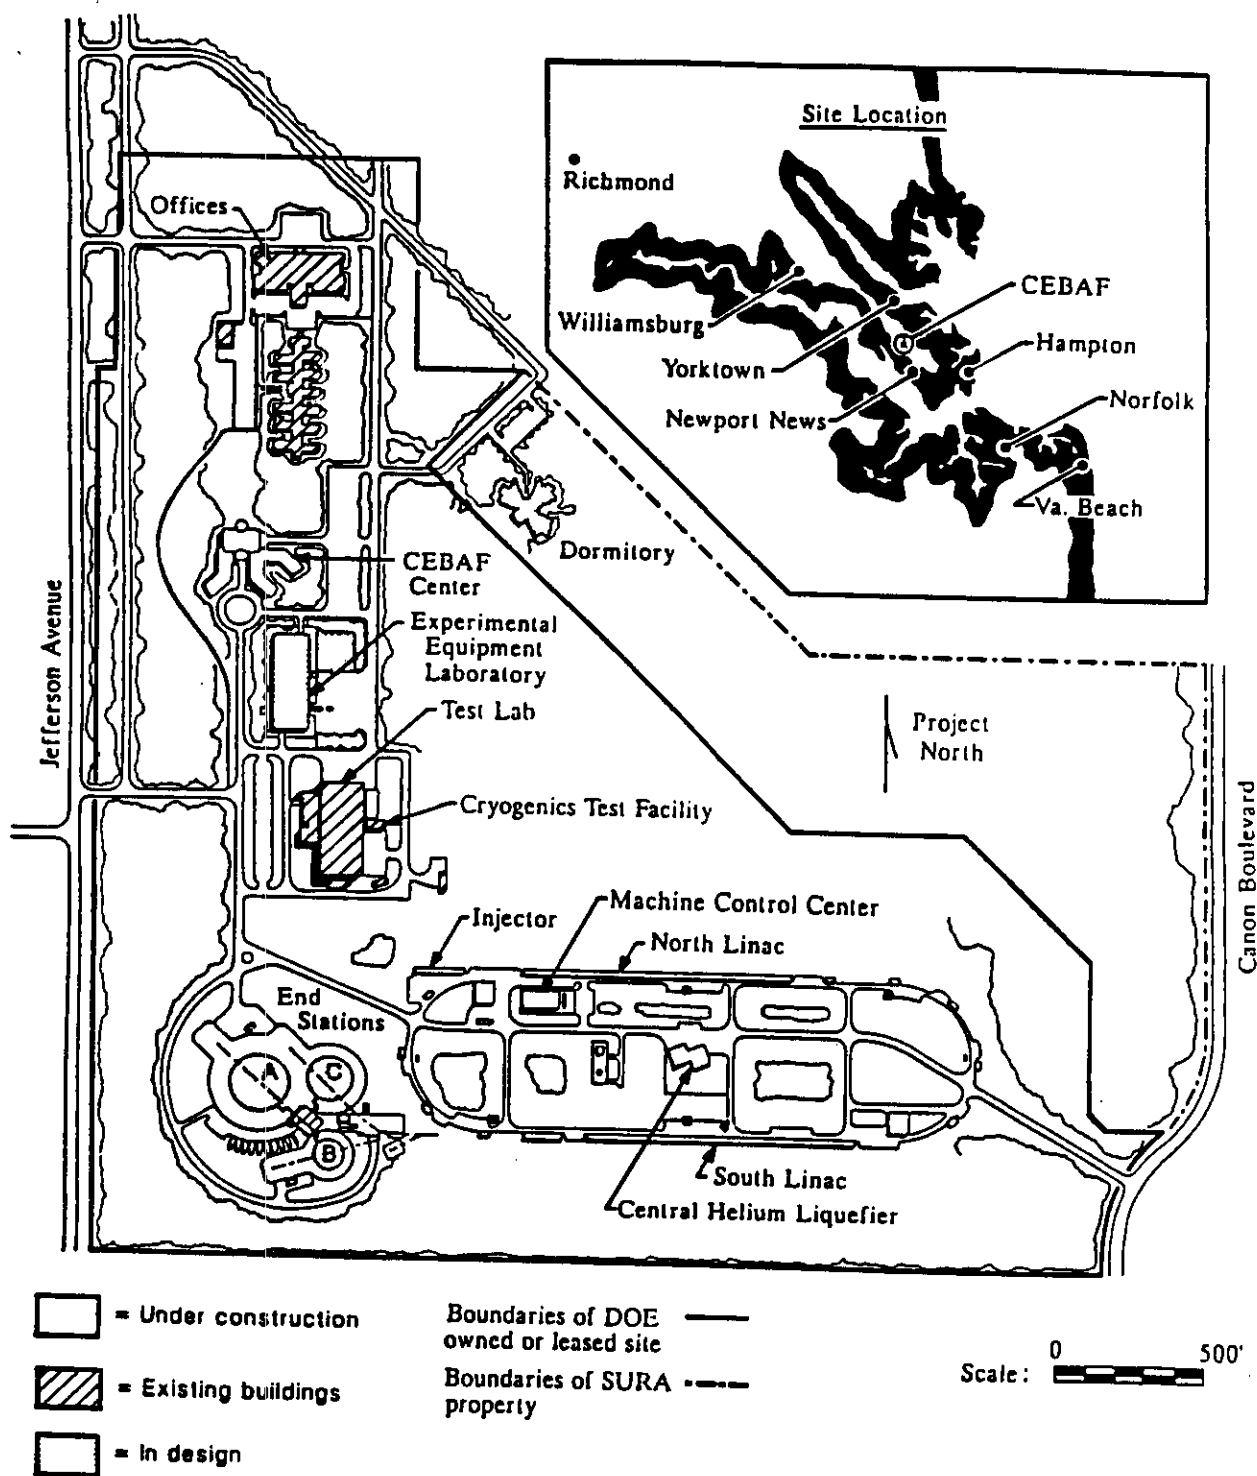


Figure 1 CEBAF's site plan. The superconducting recirculating accelerator will serve nuclear physics experiments in three end stations. The experimental equipment laboratory will support detector assembly and related work, and the dormitory will accommodate visiting experimenters.

Performance objectives are:

Energy	$0.5 \leq E \leq 4.0 \text{ GeV}$
Beam current	$I \leq 200 \mu\text{A}$
Duty factor	cw
Emittance	$\epsilon \approx 2 \cdot 10^{-9} \text{ m}$
Momentum spread	$\sigma_E/E = 2.5 \cdot 10^{-5}$
User multiplicity	3 beams

The 200- μA total output current can be distributed in controllable ratios between three end stations (Figure 2). The emittance is unnormalized and refers to the full beam size, i.e., $\sigma_x^2 = \frac{1}{4}\epsilon_x\beta_x$. The value of $\epsilon = 2 \cdot 10^{-9} \text{ m}$ at 1 GeV is equivalent to $\epsilon_N \approx 10^{-6}$ m in storage ring terminology (i.e., $\sigma_x = \epsilon_{N,x}\gamma\beta_x$). Due to various emittance-degrading effects we do not quote the normalized emittance: $\epsilon < 2 \cdot 10^{-9} \text{ m}$ at $E > 1 \text{ GeV}$ is neither precluded nor guaranteed.

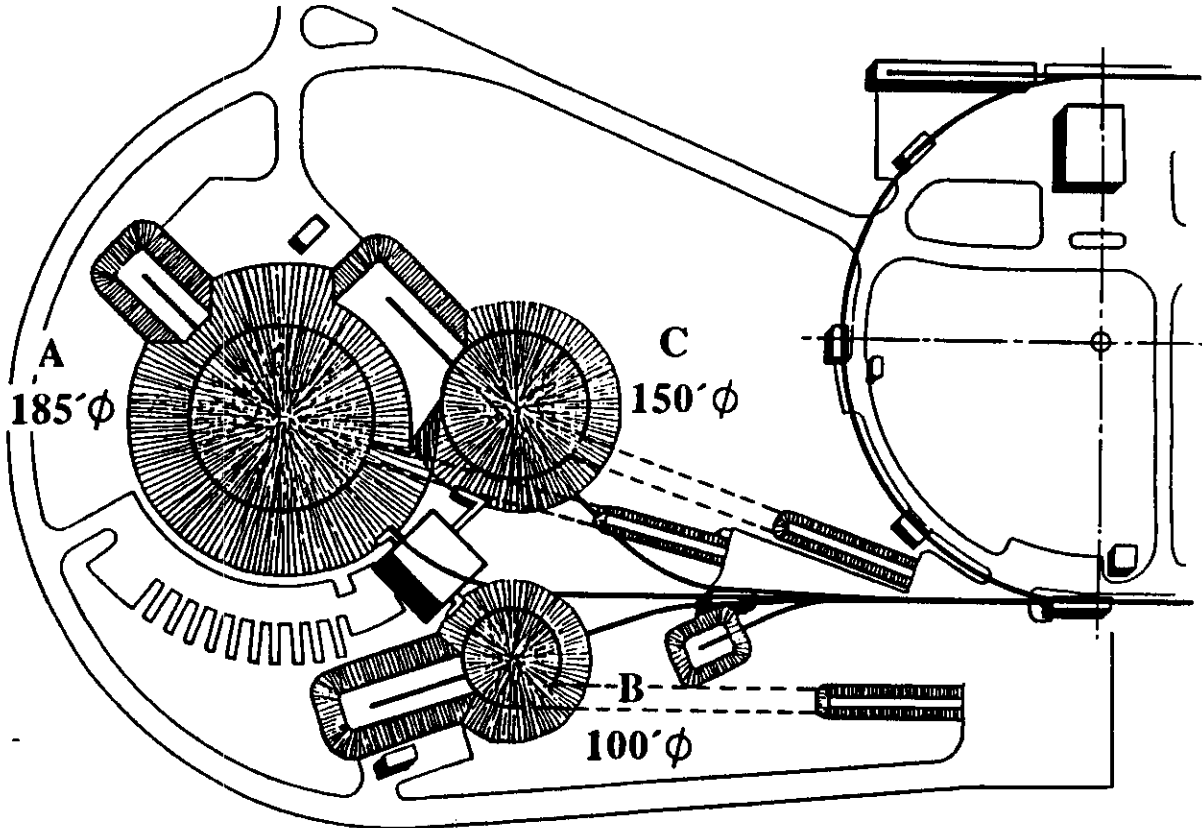


Figure 2 Plan view of CEBAF's three end stations, showing beamlines from the superconducting recirculating accelerator and truck ramps for equipment access. Support facilities will include a counting house (*center*) with one counting room per end station, and parking for users' trailers.

First beam to an experiment is scheduled for 1994. This paper outlines the growth and progress of CEBAF's planned program of nuclear science, and then describes the accelerator and reports its construction status.

Nuclear Physics Research at CEBAF

CEBAF will be a user facility—a research tool for the nuclear physics community. In parallel with the efforts to design and construct the accelerator, CEBAF has from the beginning collaborated with the national and international user community to plan experiments and the necessary instrumentation to exploit the accelerator's capabilities. The present status of the planning for each end station is summarized below, followed by a description of the scientific program planning process and CEBAF's physics outlook.

End Station A An important part of the CEBAF physics program involves completely exclusive experiments in which the nuclear final state has to be fully specified. The physics program of Hall A will therefore include:

- Measurement of elastic and inelastic form factors.
- $(e, e'N)$ reactions for study of single-nucleon density distributions, momentum distributions at high momenta, and the electromagnetic structure of bound nucleons.
- $(e, e'd)$, (e, e'^3He) , $(e, e'2N)$ reactions to specified final states (multinucleon correlations).
- $(e, e'\pi)$ reactions (nucleon and nuclear pion fields).
- $(e, e'K)$ reactions for preliminary hypernuclear physics investigations.

A pair of 4-GeV/c high-resolution ($\delta p/p \leq 10^{-4}$) spectrometers with moderate acceptance (~ 8 msr) will be used to carry out this experimental program. Table 1 lists the main optics design characteristics. Figure 3 shows a side view of such a spectrometer.

Table 1
Main Optics Design Characteristics
4-GeV/c QQDQ Spectrometer

Maximum momentum	4 GeV/c		
Total bending angle	45°		
Optical length	25 m		
Configuration	vertical		
Momentum acceptance	$\pm 5\%$		
Momentum dispersion	14.3 m		
Radial magnification	-2.6		
$ D/M $	5.1 cm/%		
Momentum resolution	$< 10^{-4}$		
Angular acceptance horiz.	± 30		
(mr.) vert.	± 65		
Solid angle (msr)	7.8		
Horizontal angular resolution	< 0.5 mr		
Transverse length acceptance	± 5 cm		
Transverse position resolution	< 0.15 cm		
Quadrupoles:	Q_0	Q_1	Q_2
Bore radius (m)	0.15	0.26	0.31
Pole tip field (T)	0.84	0.81	0.91

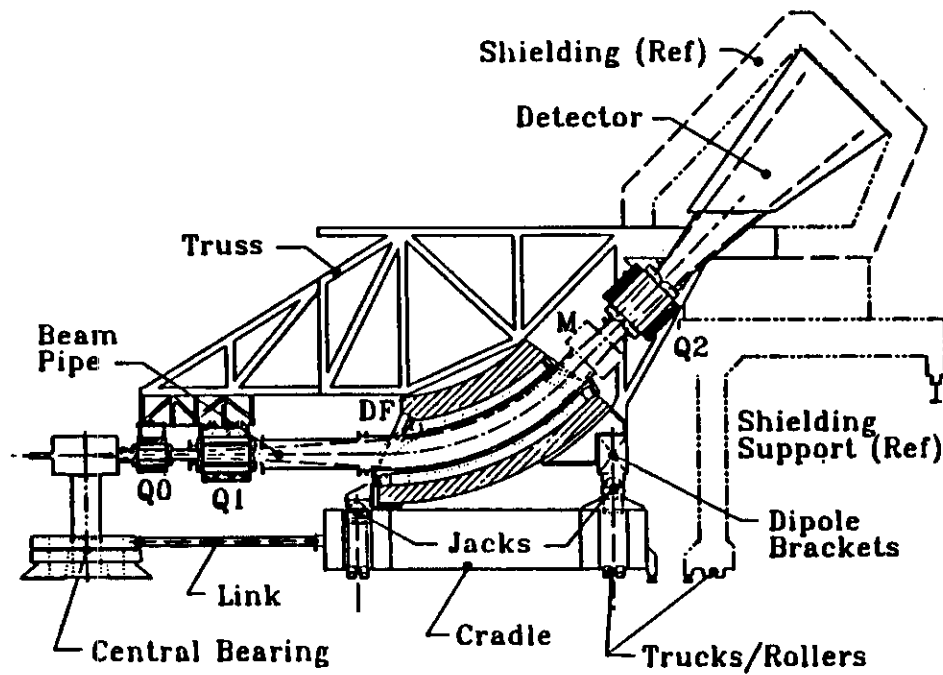


Figure 3 Side view, 4-GeV/c high-resolution spectrometer.

The hall (Figure 4) will have an interior diameter of 185 ft, a trench for a future out-of-plane beam, equipment access via a truck ramp, and a 20-ton overhead crane. The spectrometers will rotate around a common axis on rigid support structures traveling on concentric rails.

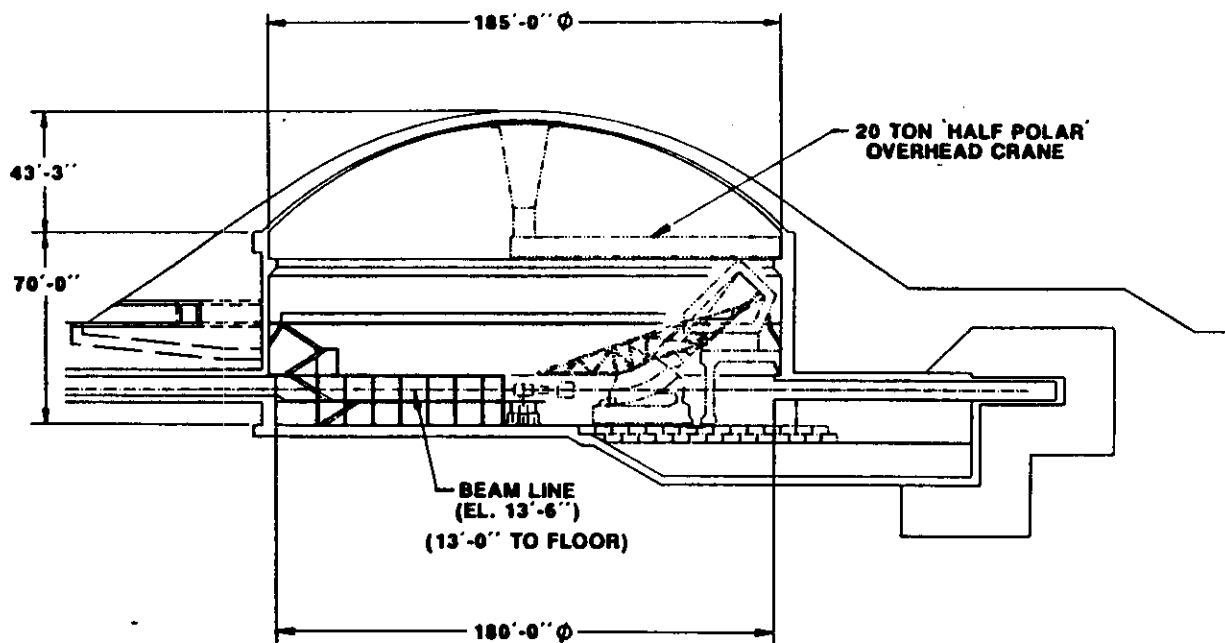


Figure 4 Elevation view, End Station A.

Co-program managers for Hall A are CEBAF's Jean Mougey (formerly of Saclay, France) and Robert Lourie of the University of Virginia. The spectrometers will cost approximately \$20 million and will require approximately 100 manyears from users and 100 manyears from CEBAF to build.

End Station B The Hall B program will include:

- Bias-free investigation of hadronic final states X in inelastic electron scattering; i.e., $(e, e'X)$, $X = N, \pi, N + \pi, N + N$.
- Detection of multiple-particle final states; e.g., electromagnetic transition form factors of 3-quark systems, resonance production and propagation in nuclei, and multi-nucleon emission.

A large acceptance spectrometer (LAS) will carry out this program. The multi-gap device will be based on a toroidal magnet (Figures 5 and 6) with six superconducting coils arranged around the beamline to produce an essentially circular magnetic field. The LAS will cover a large angular and momentum range for charged particles, photons, and neutrons, and will have moderate momentum and angular resolution and good particle identification capabilities. The particle detection system consists of drift chamber superlayers to determine charged-particle tracks, scintillation counters for the trigger and for time-of-flight measurements, and shower counters to detect electrons and photons. The six segments are individually instrumented to form six independent magnetic spectrometers. The high luminosity and count rate capability of the LAS will be important for investigation of processes with small cross sections. Use of the LAS with polarized targets and neutron counters with long flight path will broaden the Hall B program. Table 2 enumerates the key features and performance characteristics of the LAS.

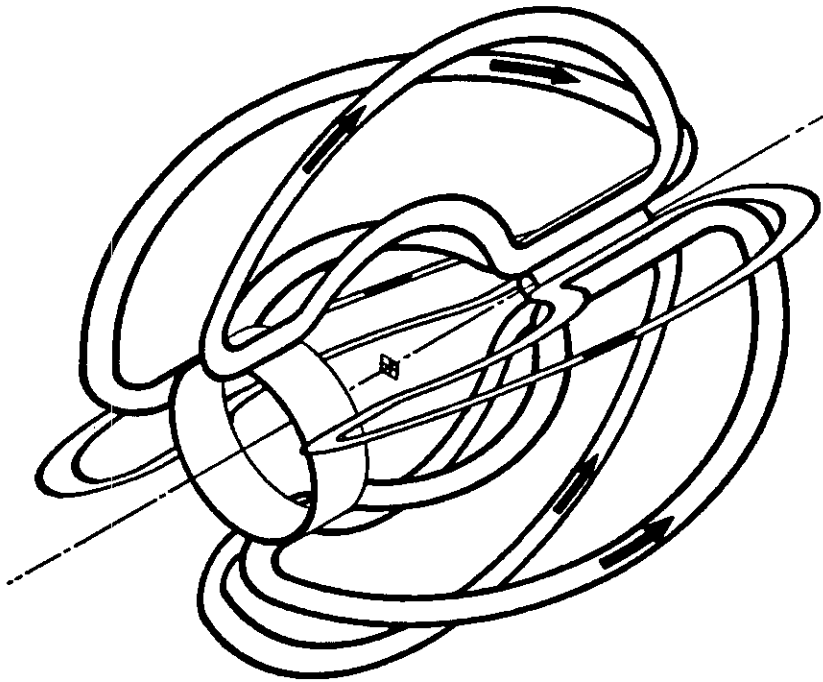


Figure 5 Six-coil torus configuration.

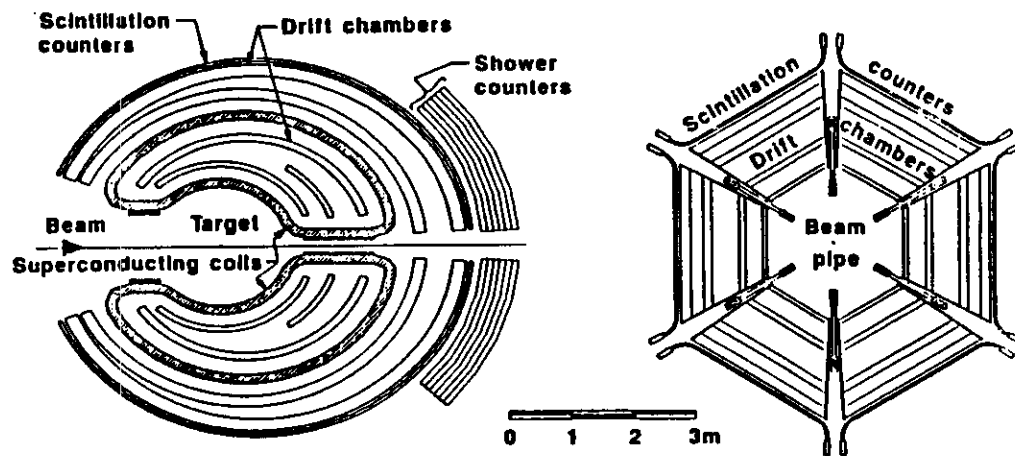


Figure 6 Large acceptance spectrometer (LAS), side and longitudinal views.

Table 2
Large Acceptance Spectrometer
Key Features and Performance Characteristics

- Toroidal magnetic field from six superconducting coils
 - $\int B dl$ $\sim 3.5 \text{ Tm at } 10^\circ \theta$
 - $\sim 0.8 \text{ Tm at } 90^\circ \theta$
 - Max field $\sim 2.5 \text{ T}$
- ϕ -Acceptance $50\% \text{ at } 10^\circ \theta$
- $85\% \text{ at } 90^\circ \theta$
- Five superlayers of hexagonal drift cells
- $\sim 40,000$ active wires
- $L \geq 10^{34} \text{ cm}^{-2} \text{ sec}^{-1}$
- Flexible pre-selection electronics to avoid taping uninteresting events

Figure 7 is an artist's conception of the LAS in Hall B. The hall is planned to have an inside diameter of 100 ft, equipment access via a truck ramp, and an overhead crane. Space will be provided to move the LAS aside for tagged photon beam experiments.

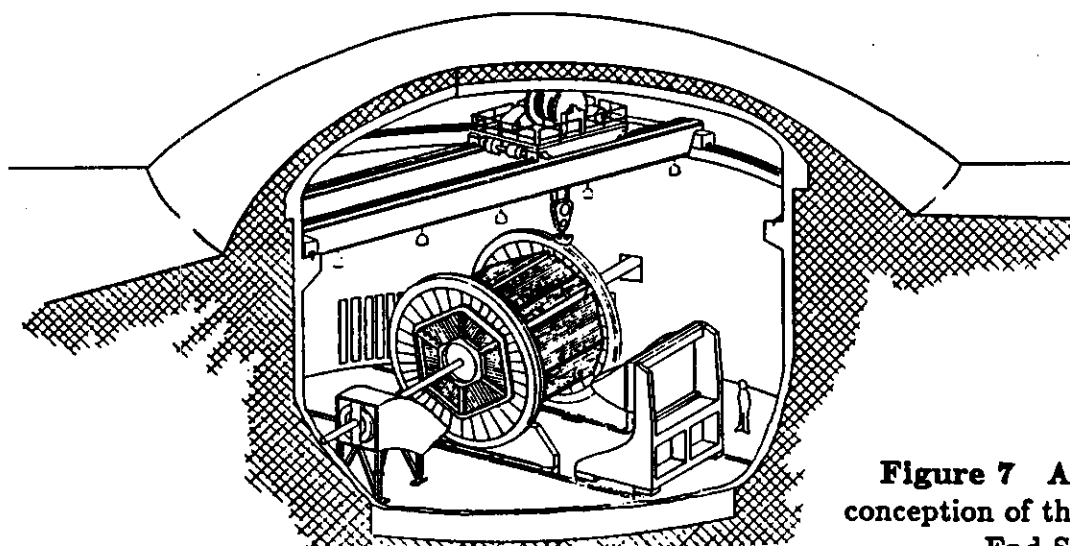


Figure 7 An artist's conception of the LAS in End Station B.

Co-program managers for the LAS are Bernhard Mecking of CEBAF and Robert McKeown of the California Institute of Technology. Estimated cost of the device is \$18 million; estimated manpower requirements to build it are 240 manyears, with half coming from among the users.

End Station C Hall C is envisioned as serving a diversity of physics interests, including:

- Form factor measurements, with accurate measurement of G_{En} as a function of Q^2 .
- Parity violation investigations, with precision tests of extensions to the standard model in the electron-quark sector.
- A high- Q^2 baryon resonance program to test predictions of perturbative QCD.

Devices planned to carry out the Hall C program include a moderate-resolution, high-momentum, 6-GeV/c spectrometer and several specialized second arms such as

- a symmetric toroidal array spectrometer (STAR),
- a hypernuclear spectrometer,
- a short-orbit spectrometer, and
- a non-focusing spectrometer.

The STAR is shown schematically in Figure 8. Based on an eight-sector toroidal design, it will be a large solid angle, high-luminosity device with a convergent focal area. The STAR will be used for out-of-plane measurements, parity violation measurements, "180°" (e, e'), and ($e, e'2N$).

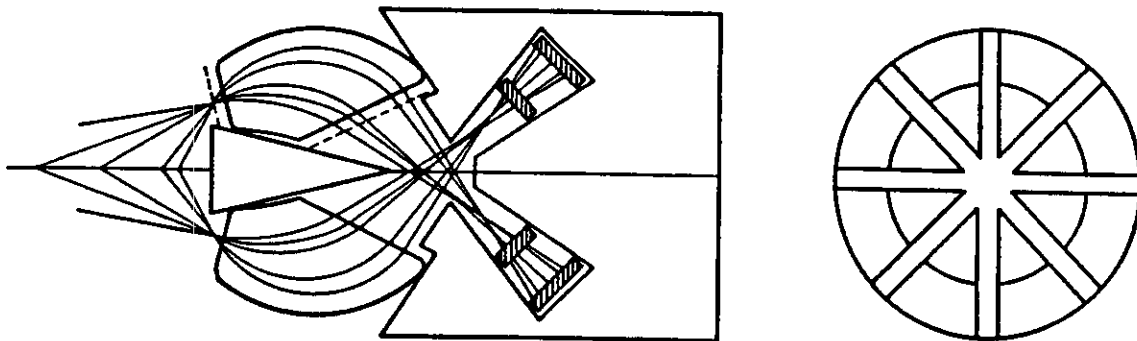


Figure 8 Side and longitudinal schematic views, symmetric toroidal array spectrometer (STAR) for End Station C.

Figure 9 is an artist's conception of Hall C configured for studies using the high-momentum spectrometer and the STAR. Hall C will have a diameter of 150 ft, with the beamline passing through the hall off center in order to accommodate the planned combinations of equipment. A truck ramp will provide equipment access.

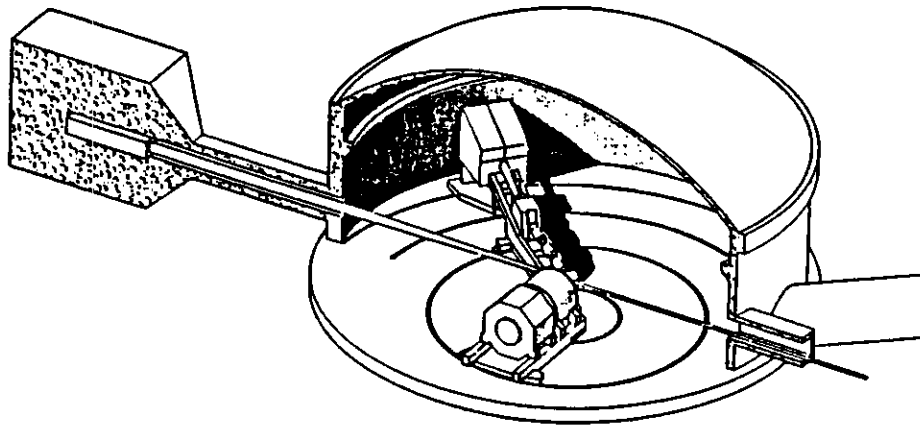


Figure 9 Artist's conception of the high-momentum spectrometer and the STAR in End Station C.

Co-program managers are Roger Carlini of CEBAF and Lawrence Cardman of the University of Illinois. The combined cost of the initial complement of devices is estimated to be \$19 million. Approximately 250 man-years will be needed to build the devices, with about 2/3 of the effort coming from users.

Scientific Program Planning and Physics Outlook The envisioned program of nuclear science has driven the instrumentation design and end station civil construction design. Workshops, summer studies, task forces, and other formal and informal collaborative efforts since early in the 1980s have advanced the interlinked planning for physics experiments and for equipment and facilities. In 1987, the Program Advisory Committee (PAC) was formed to advise CEBAF on the direction and progress of scientific program planning. Table 3 lists the current PAC membership. Also in 1987, Technical Advisory Panels (TAPs) were formed to provide detailed technical guidance on equipment for specific halls, and a first round of letters of intent (LOI) was received from prospective users. These 61 letters from 192 prospective users at 50 institutions outlined initial plans for specific experiments at CEBAF.

By late 1988, a year that saw 18 different scientific program planning meetings of CEBAF staff and users, the partnership between CEBAF and the nuclear physics community had produced

- a second round of letters of intent—90 LOI from 233 physicists at 58 institutions in 7 countries,
- preliminary conceptual designs of experimental equipment to carry out such experiments, and
- a conceptual design report for the civil construction of the end stations, planned as domed buildings whose circular shapes maximize usable floor space for experimental equipment.

By early 1989 the CEBAF User Group numbered 676. In February 1989, the PAC reviewed the second-round LOI and the experimental equipment preliminary designs, and endorsed the overall planning for the three halls' complementary programs of research.

Thus CEBAF's present scientific program planning focus is on planning and prioritizing the experiments in detail, finalizing the designs, and building the equipment. This effort will require massive participation by the scientific users. Three collaboration meetings were held in the first two months of 1989, and CEBAF is calling for collaborations to form to submit detailed proposals for physics research, to complete experimental equipment conceptual designs, to build detector subsystems at home institutions, to provide over 300 man-years of scientific program preparation effort beyond that contributed by CEBAF staff, and to provide about \$25 million in equipment. The PAC will meet later this year to review and approve proposals and to recommend CEBAF's initial experiments.

More detailed information, including the Experimental Equipment Preliminary Conceptual Design Reports and the End Station Civil Construction Conceptual Design Report, is available from CEBAF. The collaborations are now forming, and are actively seeking new members to contribute to preparations for, and later to take part in, experiments at CEBAF. International participation is welcomed.

Table 3 CEBAF Program Advisory Committee

J. Schiffer, Chairman (Argonne)	
R. Arnold (American University)	P. Barnes (Carnegie-Mellon)
W. Bertozzi (MIT)	T. W. Donnelly (MIT)
R. Eisenstein (Illinois)	S. Fantoni (Pisa)
J. Friar (Los Alamos)	B. Frois (Saclay)
H. Jackson, ex officio (Argonne)	S. Kowalski (MIT)
E. Moniz (MIT)	I. Sick (Basel)
H. Thiessen (Los Alamos)	S. Wojcicki (Stanford)

Accelerator Design

A true cw device is the approach of choice to produce a high-quality continuous beam. Low peak current for a given average current lowers emittance, and continuously operating rf systems can be controlled more precisely in both phase and amplitude, thereby leading to smaller energy spread and smaller variations of average energy. The conceptually simplest approach would be a straight linac, and the most mature technology that of room temperature rf structures operating in the range of 1500 to 3000 MHz. This approach, however, leads to excessive power consumption (~ 100 MW for GeV-range beams) and high capital cost. At a gradient of 5 MV/m, assuming cavity Q -values in the 10^9 range and cryogenic plant efficiencies of $\sim 10^{-3}$, total power dissipation for a superconducting linac translates into wall plug power of a few kW/m of accelerating structure. This lowers power consumption into a more realistic realm, but even then a straightforward superconducting

linac of 4 GeV would not be the most effective approach in terms of either operating costs or initial capital expense. A last optimizing step is accomplished through recirculation, i.e., the repeated passing of the beam through the same accelerating section.

The CEBAF Recirculating Linac Concept Figure 10 illustrates schematically the CEBAF recirculating linac concept. Four-pass recirculation was originally chosen in 1985 as being close to the cost minimum and of acceptable complexity. In spring 1988, however, reevaluation of the cost and complexity issues resulted in a change to five-pass recirculation. Total accelerator circumference is minimized by splitting the acceleration structure into two equal segments located in the straight sections of the racetrack configuration.

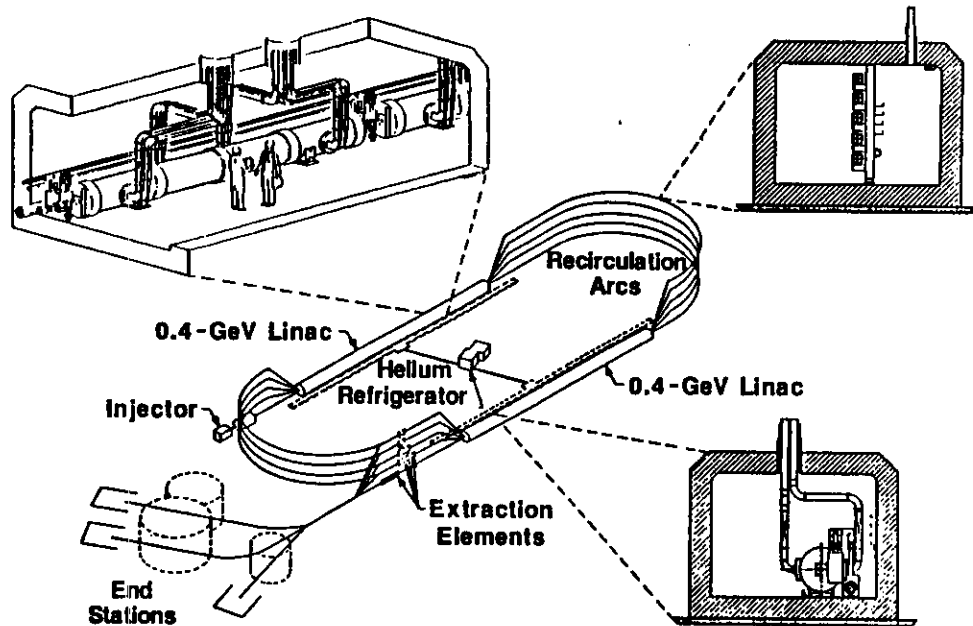


Figure 10 Schematic diagram of the CEBAF superconducting, five-pass recirculating linac. The cutaway shows $1\frac{1}{4}$ cryomodules in the tunnel. Four cryounits, each containing a cavity pair, comprise each cryomodule. Cryounits are fed rf power alternately in a right-left-left-right pattern.

The beam transport lines connecting the two linac segments are achromatic and isochronous, provide matching in all phase space coordinates, and are designed with adequate bend radii and strong focusing to minimize quantum excitation to preserve the high beam quality.

The entire machine is operated in true electron linac mode, i.e., with the particle bunches "riding the crest" of the sinusoidal rf wave shape without longitudinal focusing, relying on the extreme relativistic motion of the electrons.

Fundamental Design Choices Among the fundamental choices in the design of a large recirculating linac, in addition to the number of recirculations, are rf frequency and the average radius of the recirculating arcs.

Given the complex and exacting nature of the superconducting cavities, the long development time for each of today's successful examples, and the potential schedule impact

of departures from proven design, the choice of frequency furthermore implies the choice of a very specific design. CEBAF's adoption of the 1500-MHz Cornell design rested on the availability of a proven design and on the acceptability of a 500-MHz time structure (1500 MHz split three ways) for the nuclear physics experiments.

The radius of the arcs is determined by the maximum energy and the expected beam quality, i.e., by how much degradation due to synchrotron radiation is tolerated. With many leaders in the nuclear physics community discussing the potential experimental opportunities in the 10- to 20-GeV range, CEBAF sought to make no design choices that would preclude later upgrade to such energies. The arcs were therefore laid out, loosely packed with dipoles, such that by installation of a more tightly packed lattice with larger magnetic radius, beams in that energy range could be transported with satisfactory degradation of emittance and momentum spread.

The CEBAF Design: Systems Highlights

Table 4 summarizes the CEBAF accelerator parameters.

Table 4
Design Parameter List
CEBAF Superconducting Radio-Frequency CW Linac

Beam characteristics

Electron energy E	$0.5 \leq E \leq 4.0$ GeV
Average current	200 μ A
Transverse emittance (95%, 1 GeV)	2×10^{-9} m
Energy spread (95%)	1×10^{-4}
Duty factor	100% (cw)
Simultaneous beams	3

Linac parameters

Concept	Superconducting cw recirculating linac
Number of passes	5
Number of linac segments	2
Maximum energy gain per pass	0.8 GeV
Recirculation time per pass	4.2 μ s
Focusing	FODO
Phase advance per cell (pass 1)	120°
Half-cell length	9.6 m
Cavities per half-cell	8
Half-cells per segment	20
Vacuum (before cooldown)	10^{-9} Torr

Cavity parameters

Type	Superconducting
Frequency	1497 MHz
Electric length	0.5 m
Shunt impedance (r/Q)	960.0 Ω/m
Design gradient	5.0 MV/m
Design Q_0 at 2 K, 5 MV/m	2.4×10^9
Typical HOM Q_{external}	10^3 to 10^5
Clear aperture	70 mm
Transverse HOM $Z''T^2/Q$	$\leq 16.4 \times 10^4 \Omega/\text{m}^3$
Loaded Q (fundamental mode)	6.6×10^6

Superconducting structures rf system

Number of klystrons	338
Klystron power rating	5.0 kW
Phase control	$<1^\circ$
Gradient regulation	$<10^{-4}$

Injector parameters

Gun energy	0.10 MeV
Injection energy	45 MeV
Current	200 μA
Transverse emittance (at 0.1 MeV)	1 mm·mr
Longitudinal emittance	$<15 \pi \text{ keV} \cdot \text{degrees}$
Bunch length at 45 MeV	$<1.0^\circ$
Pulse capability	0.05 to 10 μs

Recirculation arc beam lines

Number	9
Magnetic radii	5.1 to 30.6 m
Phase advance per period	$2 \pi(5/4)$
Periods per arc	4

Cryogenic system

Total rf load (2.0 K)	2050 W
Total heat load (2.0 K)	2700 W
System capacity (2.0 K)	4800 W
Total heat load (45 K)	8000 W

Injector The injector provides a high-quality electron beam that is sufficiently relativistic (nominal 45 MeV) to stay in phase with the rf and the recirculating electron beams in the first half of the linac. The bunching, capture, and initial acceleration (up to 0.5 MeV) regions utilize room-temperature technology and are modeled after proven injector

designs. This beam is further bunched and accelerated to just over 5 MeV in two five-cell superconducting cavities in a short cryostat, and then accelerated in two full-sized cryomodules to the required 45 MeV before injection into the linac. At the nominal injection energy of 45 MeV, total phase slip (with respect to a reference particle moving at $\beta \equiv 1$) is less than 2° , through five passes, most of which occurs in the first half of the first pass through the first segment.

The entire injector up to 5 MeV has been modeled with PARMELA, a two-dimensional particle simulation code that calculates phase and radial properties, including space charge effects, for an electron beam. Calculations indicate that a bunch of less than 1° phase angle at 1.5 GHz and 20 keV full width should be obtained at the exit of the injector. The injector enclosure has been designed to accommodate two electron guns so that in the future both polarized and unpolarized beams can be provided.

Acceleration Systems: Cavities, Cryogenic System, and RF System The five-cell, 1497-MHz, elliptical cavities (Figure 11) developed at Cornell University and adopted for CEBAF provide suitable frequency, gradients in excess of 5 MV/m in laboratory and beam tests, damping of HOMs, and technical maturity, i.e., readiness for industrial prototyping and production. The cavities operate in the π mode, and have a fundamental coupler on the beamline at one end and an HOM (higher order mode) coupler on the beamline at the other. The elliptical shape yields low peak surface electric fields, a good chemical rinsing geometry, and good mechanical rigidity. The HOM coupler has two orthogonal waveguides for extraction of HOMs. HOM Q 's are typically in the range of $500 < Q_{\text{HOM}} < 170,000$, which represents five orders of magnitude of damping. Each linac segment contains 80 m active length in the form of 160 cavities, providing 0.4 GeV energy gain per segment at a gradient of 5 MV/m. Eight cavities are combined in each cryomodule, each of which is connected to its neighbor by a warm section containing beam vacuum pipe, vacuum equipment, beam monitors, and magnetic elements (quadrupoles and steering dipoles) to focus and guide the beam.

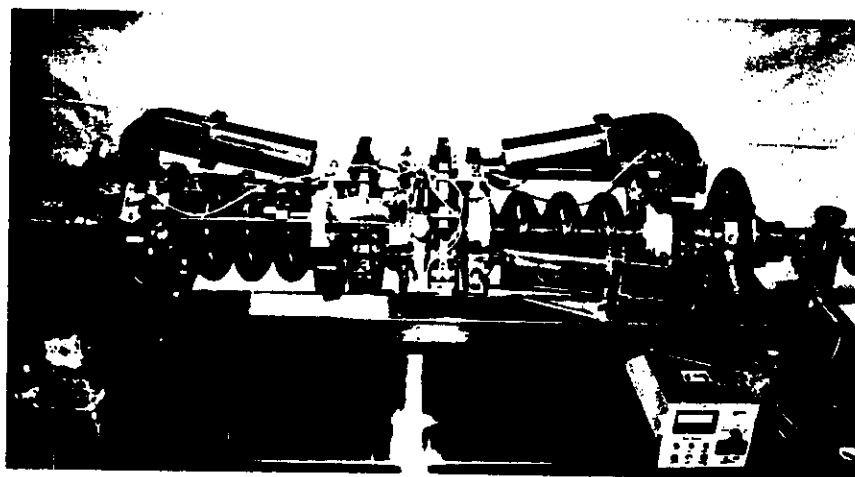


Figure 11 A CEBAF-Cornell cavity pair.

The operating temperature was selected on the basis of a cost optimization study. Liquid helium refrigeration systems become more expensive (capital and operating costs) as

their design temperature decreases. Yet rf heat losses in the cavities increase exponentially with temperature. For CEBAF the optimum is around 2.0 K.

The cryogenic system for CEBAF consists of a 4.8-kW central helium refrigerator and a transfer line system to supply 2.2-K, 2.8-atm helium to the cavity cryostats, and 38-K helium at 4.0 atm to the radiation shields. The 2.2-K helium is expanded by Joule-Thompson (JT) valves in the cryostats, yielding 2.0 K at 0.031 atm. The central helium refrigerator will be located in the center of the CEBAF racetrack with the transfer lines located in the linac tunnels.

The superconducting structures rf system consists of 338 individual rf amplifier chains (Figure 12). Each superconducting cavity is phase-locked to the master drive reference line to within 1° , and the cavity field gradient is regulated to within <1 part in 10^4 by an rf control module. Continuously adjustable, modulo- 360° phase shifters are used to generate the individual phase is used for level feedback. The close-coupled digital system enhances system accuracy, provides self-calibration, and continuously checks the system for malfunction. Calibration curves, the operating program, and system history are stored in an on-board electrically erasable programmable read only memory (E²PROM). The rf power is generated by a 5-kW, water-cooled, permanent-magnet-focused klystron. The klystrons are clustered in groups of eight and powered from a common supply.

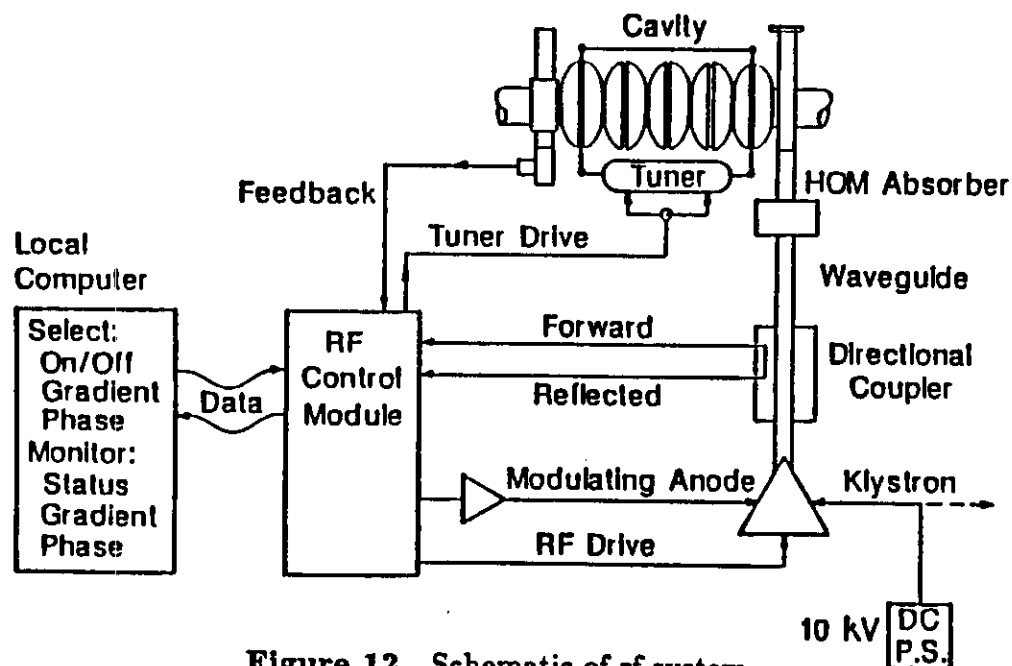


Figure 12 Schematic of rf system.

Energy spread and deviation of central energy from nominal operating value depend on control of bunch length from the injector, as well as of phase and amplitude of the accelerating field. With 320 cavities in the linacs, careful distinction between correlated and uncorrelated errors is necessary. It was found that some tolerances for the individual control modules can be reduced if a feedback loop for overall amplitude, based on beam measurements in a high-dispersion section of the lattice, is used. Requirements still remain stringent with maximum uncorrelated rms errors of a few 10^{-4} in voltage and at most a

few degrees in phase. Correlated rms errors must be kept to below $2.2 \cdot 10^{-5}$ in amplitude and 0.24° in phase.

Over the entire planned current range, ~ 0 to $200 \mu\text{A}$, gradients up to $\sim 10 \text{ MV/m}$ can be achieved with 5 kW incident power. At the chosen Q_L of $\sim 6.6 \cdot 10^6$ a perfect match exists for $160 \mu\text{A}$ (through five passes) at 5 MV/m , and a good match at 10 MV/m ; at lower current power is reflected.

Beam Transport and Optics Beam transport channels can be classified into the beam switchyard (BSY), distributing beam to the end stations, and the accelerator internal transport elements. Looking at the latter, we can distinguish between the linac focusing structure and the nine recirculation half-arcs, five at the accelerator's east end, and four at the west end.

The linac optics are set up as a simple FODO channel with half-period length of 9.6 m with constant 120° phase advance along the full length of the first pass. Viewed from the linac, all east arcs are essentially "invisible," i.e., they represent isochronous, achromatic identity transformations. On the second and later passes, focusing is weaker given the higher particle momentum, and phase advance per cell is no longer a constant. Therefore, there exists no longer a unique matched set of β -functions, and a continuum of input conditions over a relatively broad range results in a satisfactory beam envelope through the linac. Correspondingly, the west arcs are tuned to more general transformations in the transverse phase space while retaining the features of isochronicity and achromaticity.

The structure of each arc arises from five distinct regions: spreaders, matching/extraction region, arcs proper, matching region, and recombiners. Spreaders and recombiners are achromatic, vertical, double bends. The lattice design executes the vertical displacement in a staircase fashion. This requires weak quadrupoles to achieve achromaticity as well as low β -functions, which together minimize sensitivity to quadrupole alignment errors and vibrations. Matching and matching/extraction sections are straight sections containing quadrupoles to match β -functions into (or from) the arcs proper from the spreaders (or into the recombiners). Path-length-adjusting "dog legs" are located in the matching/extraction regions, and extraction gear is installed in the west region with the east region remaining for future expansion.

The arcs proper, isochronous and achromatic, are based upon the second-order achromat principle, made up of a periodic array of cells, synchrotron lattice fashion. Lower-energy arcs contain fewer dipoles, but have essentially the same focusing structure. Recent refinements have led to vertical stacking of all arcs with key elements occupying identical, or almost identical, horizontal locations.

The multi-user beam distribution system has two key elements: the injector and the rf-separator (deflecting cavities) in the extraction line. The injector creates three interspersed bunch trains, $k + 3N$, $k = 0, 1, 2$, and $N = 0, 1, 2, 3, \dots$, where bunches with different k can have different bunch charges, i.e., currents. The rf-separator deflects the beam, the optics amplify the initial deflection, and septum magnets extract beam for simultaneous delivery to all three end stations. At an operating frequency of $\sim 1000 \text{ MHz}$ for the rf-separator and $\sim 1500 \text{ MHz}$ for the rf system, the separator phases are independent of N and amount to ϕ_0 , $\phi_0 + 240^\circ$, $\phi_0 + 120^\circ$ for bunch trains $k = 0, 1, 2$ respectively. Of particular usefulness are the initial phases $\phi_0 = 0$, leading to 0° , 240° , 120° resulting in

a "straight," "left," "right" distribution (e. g., for distributing beams of equal energy to three end stations), and $\phi_0 = 90^\circ$, leading to 90° , 330° , 210° resulting in a "one right," "two left" separation sequence to deliver beam to two end stations.

Instrumentation and Control The central elements of beam instrumentation are several hundred beam current and position monitors that are based on cavities with loaded Q -values around 1000 and operate at 2994 MHz. Profile monitors in the low-energy end in the injector area will be wire scanners, while several beam parameters, such as profile and bunch length, will be measured in the arcs with synchrotron radiation monitors.

Control system requirements are to implement setpoints, and read, analyze, and display systems values for the injector, rf including cavity parameters, beam transport and diagnostics, cryogenics and vacuum, and personnel and machine safety. The control system must provide efficient human interface for about 20,000 input/output data points. With industry standards and off-the-shelf hardware and operating system software in use wherever possible, these requirements are met by a hardware-intensive system that has a computer hierarchy of two levels, supervisory and local (Figure 13). The system can be configured with a maximum of 10 supervisory-level computers, each of which can have a subsystem of up to 20 local-level computers. Local area networks (LANs) and computer automated measurement and control (CAMAC) devices enable intelligence to be extensively distributed for automated control capabilities at the local level. This control system allows control algorithms to be put together with great efficiency. Control system applications can be quickly developed without programming, and control databases or run-time displays can be modified without requesting custom software updates.

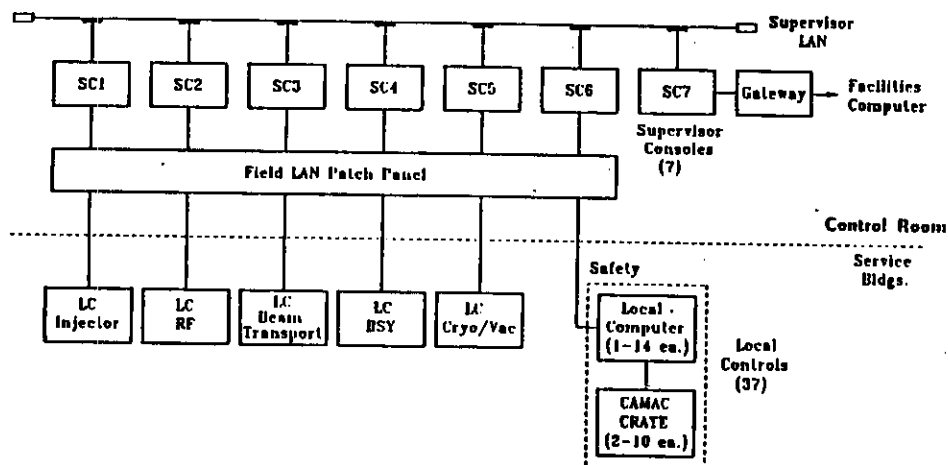


Figure 13 Control system architecture.

Issues, R&D, and Construction Progress

Key Issues and Challenges Three categories of issues and challenges have been addressed:

- The technological question of achieving reliable large-scale application of rf superconductivity, particularly in the context of a "green site" laboratory and project.
- Beam dynamics, where the primary questions pertain to beam stability and quality.

- Operability, particularly the issues pertaining to effective commissioning of this highly complex machine.

The technological issues have been addressed in three main ways. First, in July 1987 a strong SRF Technology Division was formed at CEBAF. It includes key participants from the earlier formal collaboration with Cornell. Second, a well-equipped test lab is being prepared to serve advanced R&D, to support machine operation and maintenance, and, most importantly, to support construction by providing processing, testing, assembly, and troubleshooting capability, as well as some level of fabrication capability. Third, CEBAF has pursued an aggressive industrial prototyping program for cavities and cryostats.

Test results for single cavities as well as cavity pairs (Figure 14) show that specifications can be met reliably with respect to both gradient and Q values. However, in some cases low Q values have resulted from identifiable vacuum accidents and from inappropriate chemical processing. A first cryounit has undergone initial rf and cryogenic tests at CEBAF, and tests of a four-cavity subcryomodule were completed in May 1988. In the course of this program a number of needed changes in cryostat design have been identified, including increased clearances and other improvements for cavity insertion, improved cavity-support and He vessel-alignment structures, and welded bridging components in the outer vacuum wall. The diameter of the beam pipe connecting two cavities within a pair is being reduced to lower field coupling. All these changes are viewed as straightforward. A full first cryounit of the new design is being tested in stages, and plans are to test a full cryomodule containing eight cavities by summer 1989. The procurement plan for the cavities and cryostat components is coordinated with the R&D schedule. Cavities are to be ordered in spring 1989, and different cryostat components are to be ordered following their thorough testing as prototypes.

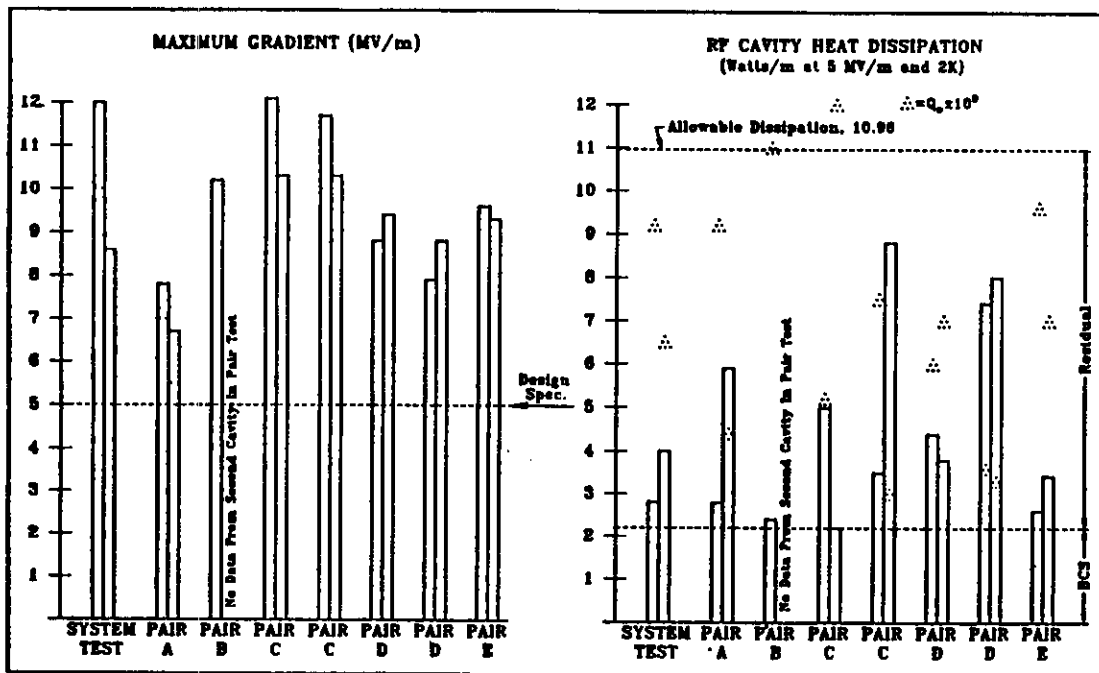


Figure 14 Prototype cavity pair test results.

Beam dynamics feasibility means primarily beam stability but also the capability to maintain beam quality under the action of a number of potentially quality-degrading mechanisms. The most important of these phenomena is the electromagnetic interaction between the beam and the "wall," i.e., the conducting boundary formed by cavities, beam position monitors, and the vacuum pipe. We can distinguish multi-bunch and single-bunch phenomena, and furthermore categorize into single and multipass phenomena. Typically the distinction between single pass and multipass is blurred or disappears for phenomena of interest in the case of intense, widely spaced bunches. For CEBAF the critically important phenomenon is multi-bunch, multipass BBU.

Two codes have been developed to analyze collective beam behavior, a 2D simulation code and a 1D "analytical" code based on matrix techniques. Both codes allow the use of realistic lattices as well as HOM frequency distributions and yield excellent agreement between them with regard to prediction of beam breakup threshold current. Threshold current was found to exceed design current by two orders of magnitude. The 2D simulation also allows study of subthreshold emittance degradation, an effect found unimportant at the few hundred μA level.

An apparent emittance degradation can occur through coupling between longitudinal and transverse phase planes, i.e., differential steering from bunch head to bunch tail. This occurs at the power couplers in the accelerating cavities where the accelerating field varies across the aperture. A "left-right-right-left" arrangement of cavity power couplers was adopted to reduce this effect and meet design specifications.

The increases in momentum spread and emittance have been mentioned previously. Synchrotron radiation introduces a momentum spread, $\sigma_E^2 \propto \gamma^7/\rho^2$, and an emittance increase, $\Delta\epsilon \propto \gamma^5\langle\mathcal{H}\rangle/\rho^2$. Here, γ has its usual relativistic meaning, ρ is the magnetic bend radius, and $\langle\mathcal{H}\rangle$ is a measure of relevant lattice properties. Generous bend radii and strong focusing (i.e. small $\langle\mathcal{H}\rangle$) control σ_E and $\Delta\epsilon$.

Operability is an area deserving early attention because CEBAF is a relatively complex device. It contains nearly 2300 magnets, nearly 2000 of which are on individual circuits; the quadrupoles, steering dipoles, and beam position monitors number over 600 each, and the total beam path length is ~ 6.5 km with a total phase advance of $\sim 150\pi$ in betatron space. Combined with a severely beam-loaded rf system requiring very precise control, this calls for early attention to operational aspects, issues, and procedures. Early commissioning (e.g., front end test of 25 to 45 MeV in 1990) and extensive computer modeling are key ingredients in our approach. Elements in facilitating commissioning and operations are a very powerful computer control system and a deliberate design philosophy of "functional modularity," i.e., an attempt to maximize one-to-one correspondence between certain components and particular actions on the beam as exemplified in the arc design.

Recent Accomplishments In addition to the cavity prototyping and cryostat development, which are now supported by the on-site liquid helium capability of a cryogenics test facility, preconstruction R&D is actively going on in magnets, magnet measurement, injector and rf separator development, beam diagnostics, and computer modeling. Major elements of the control system are in use in the test lab for cavity and cryostat testing, cryogenics control, rf tests, and injector tests. The injector gun has been thoroughly tested

at 100 keV and meets the beam quality requirements. Bunching and capture sections have been installed, and acceleration to 500 keV is scheduled for spring 1989. A beam position monitor has been bench tested, and the initial rf separator has been designed and early prototype measurements performed. An initial version of an accelerator computer model is in place, and extensive calculations, numerical and analytical, have established an initial impedance catalog for the full frequency range applicable to CEBAF's short bunches, i.e., over several hundred GHz, far beyond pipe cutoff.

Site clearing and preparation are complete, and tunnel civil construction began in summer 1988. The central helium liquefier is being fabricated by industry. Preoperations and subsystem commissioning will start in 1989. First beam to an experiment is scheduled for 1994.

Table 5 outlines key project milestones.

Table 5
CEBAF Milestones

Start construction	2Q FY 1987 (complete)
Experimental area	
conceptual design	3Q FY 1988 (complete)
Linac enclosure construction	
under way	4Q FY 1988 (complete)
Cryomodule R&D complete	3Q FY 1989
Start front end test	
(to 25 MeV)	3Q FY 1990
Start linac installation	4Q FY 1990
Start CHL operations	1Q FY 1991
Start arc installation	2Q FY 1991
Start north linac	
beam commissioning	3Q FY 1992
Construction project	
complete	4Q FY 1993
First beam to experiment	2Q FY 1994

